

SUN KID – WONDERCARPET – BELT SKD12 - 2007



DAILY CHECKLIST FOR 100 DAYS OF OPERATION

OPERATING SEASON

OWNER:

A - 6460 Imst/Tirol
 Tel (+43) 05412.68131
 Fax (+43) 05412.68132
 e-mail: office@sunkid.at
 Website: www.sunkid.at
 UID-Nr: ATU42030100

TYPE: LENGTH: MOTOR: YEAR OF MANUFACTURE:

IF PROBLEMS - CONTACT:

WEEKLY TEST (7 DAY PERIODE)

- Carefully de-icing under the driving and return drum.
- Assurance that the conveyor belt is properly tensioned and operates smoothly
- Test of the back-stop (it must not move in the locked direction)
- Check the abrasion of the belt and guide lines. Pay attention to loosen screws.

On	Date	Completed by:	Problems/check
Problems Contacted at checks			

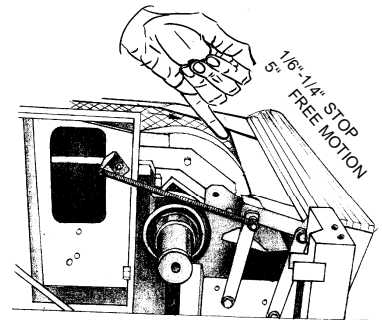
Duration of daily „ABC“-check: dependent on the length of the belt: 3 – 5 minutes.
 Yearly maintenance and gear oil change: see manual

**DAILY CHECK BEFORE OPERATION****ABC-TEST****A Check Transition Stop Device**

Using the little finger, check the function of the Transition Stop Device. Belt shall stop within 4-6 mm (1/6"-1/4") of travel. Once the stop has been initiated, the Transition Stop Device shall move freely and without obstruction until it is hidden under the unloading plate.


Check emergency stop (emergency shutdown):

Test the function of all Stop-buttons. The belt should stop!

**B Belt surface check:**

Operate the belt for at least one complete revolution, check for the following and correct as necessary:

- That no tears, rips or punctures of the belt have developed.
- That the belt tracks smoothly in the centre of the drum with minimum side-to-side movement.
- That no wires or metal pieces stick out from the splice coupling area.
- That no excessive gaps or holes exist between the snow and carpet walkways or between the belt and carpet walkways.
- That the structural integrity of the carpet-frame has not changed. With the carpet stopped, walk down the centre and check for excessive flex, bending and instability in the frame.
- That snow and ice build-up under the drive and return drums have not occurred.
- That the loading ramp to the belt is maintained level for 2-3 meters ahead of the belt.
- That the unloading ramp is slightly sloping away from the belt for 1,5 - 2 meters.
- That excessive build-up of snow and or ice on the carpet hasn't developed that could cause an user to slide backwards.
- That each carpet walkway is securely in place and locked down.

**C Monitoring Eye (optional)**

Cover up the light source: Belt must stop after 2-4 seconds

ARRANGEMENT

In case of belt damage, or a failure in the safety system stop the belt immediately, until a qualified person repairs it. If there is a failure in the Monitoring Eye it can be by-passed. For the repair time only direct supervised operation is allowed. When the weather conditions are critical, hourly, in worst case permanent inspection and maintenance of the loading and unloading area is necessary.

CHECK LIST:

1. Belt must stop after 4-6 mm (1/6"-1/4") movement of Transition Stop Device .
2. 130 mm – 5" smooth moving of the Transition Stop Device.
3. Between the belt and all covering parts (rubber, plastic, wooden covers) a maximum gap of 4 mm (1/6") is permitted (min. gap 1 mm - 1/25")
4. Belt must stop after pressing any Stop button.
5. Max. speed – stop – max. stopping distance permitted is 300 mm (12").
6. Monitor one complete revolution of the belt and check for damage.
7. The ends of the splice rods should be bent in a 90° angle in the opposite direction of belt travel. The bended ends must be inside the belt edge.
8. Monitoring Eye (optional): Belt must stop after 2-4 sec. if light source is covered.



**Any damage has to be repaired immediately!
Otherwise you risk serious accidents with injury to persons!**

If o.k. ✓	Prior to operation			Prior to after-noon operation (after 3 h)			C*Option monitoring-eye, if installed
	A	B	C*	A	B	C*	
Date							Name Tester Signature

If o.k. ✓	Prior to operation			Prior to after-noon operation (after 3 h)			C*Option monitoring-eye, if installed
	A	B	C*	A	B	C*	
Date							Name Tester Signature

Problems:
Date:

If o.k. ✓	Prior to operation			Prior to afternoon operation (after 3 h)			C* Option monitoring-eye, if installed	Name Tester Signature	If o.k. ✓	Prior to operation			Prior to afternoon operation (after 3 h)			C* Option monitoring-eye, if installed	Name Tester Signature
	Date	A	B	C*	A	B				C*	Date	A	B	C*	A		

Problems:
Date:
